


Appendix - 2

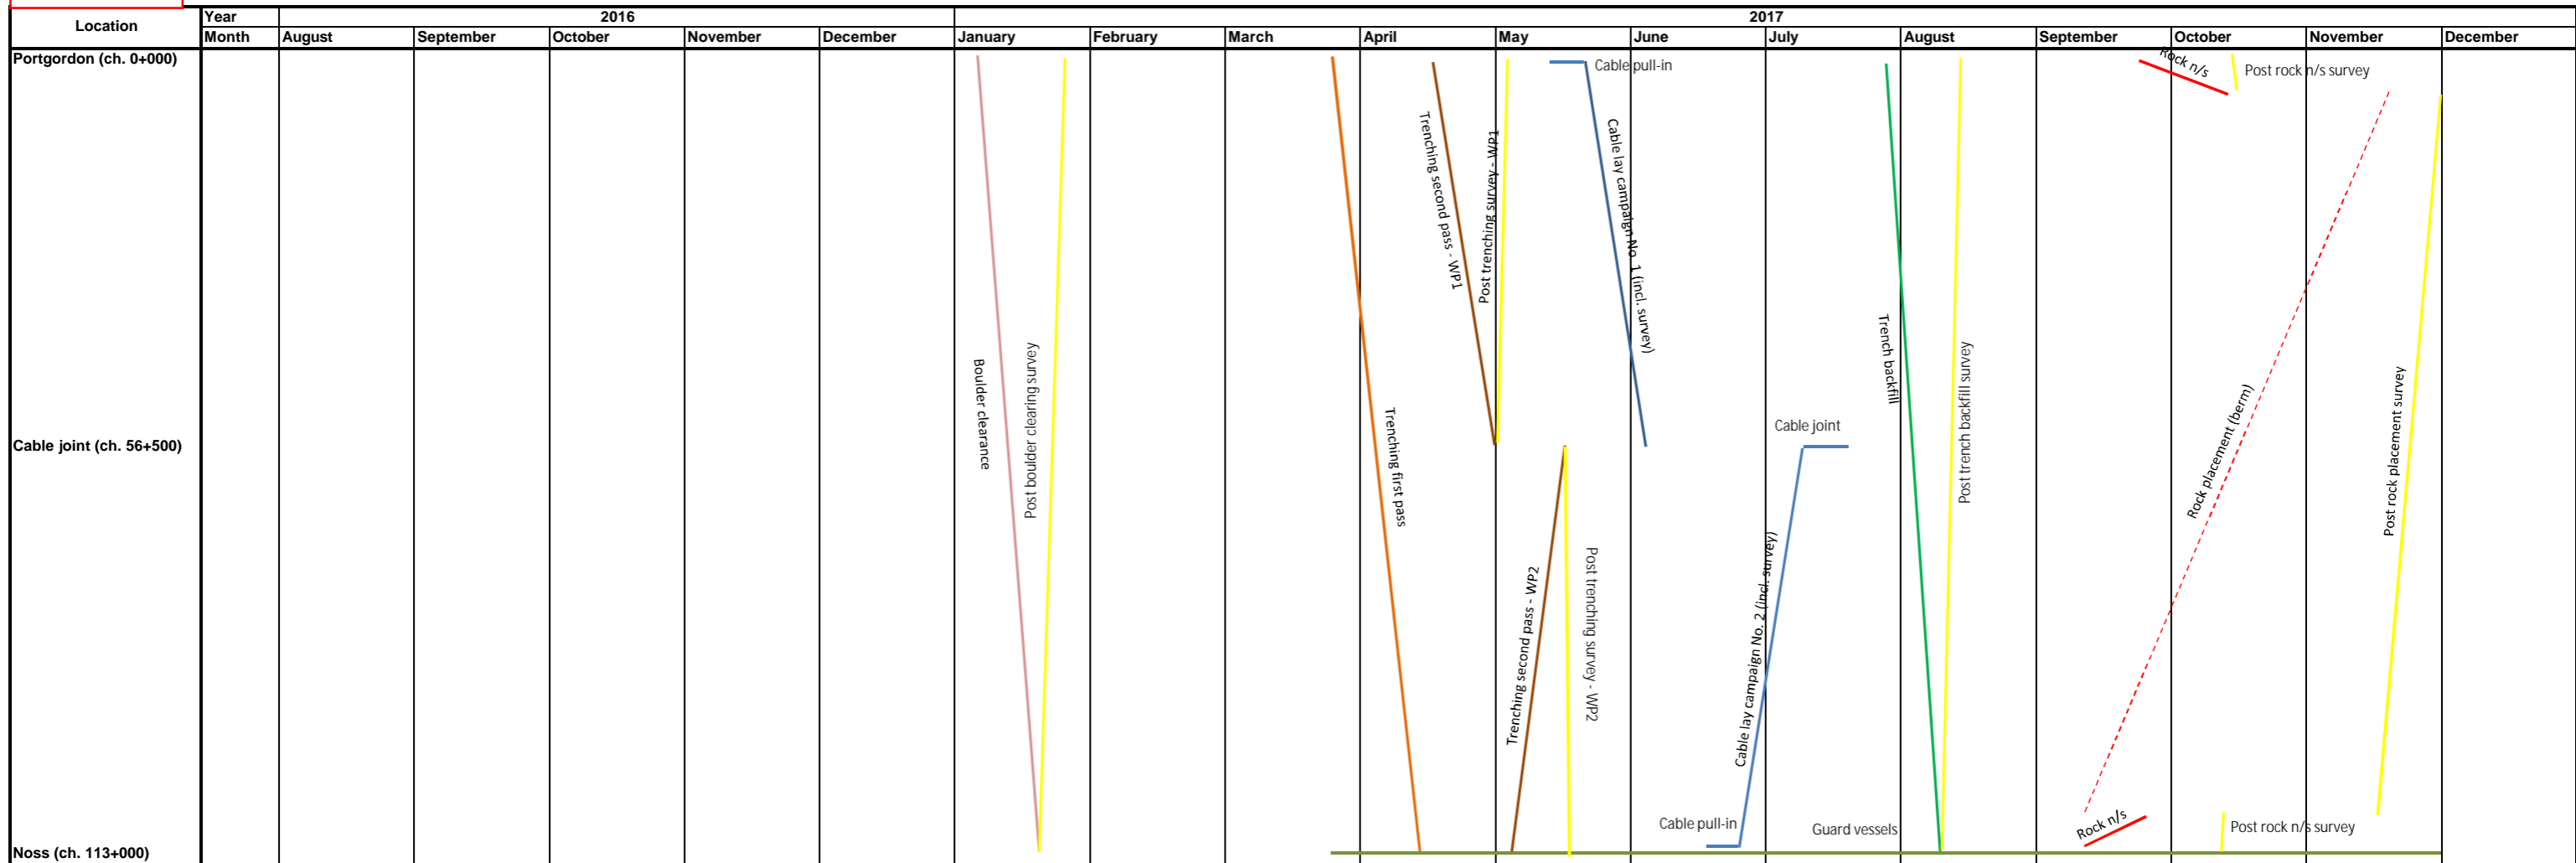

Programme dates

Activity	Start date	Finish date	Duration (days)
Boulder clearance	11/01/2017	21/01/2017	10
Post boulder clearance survey	21/01/2017	26/01/2017	5
Trenching first pass	25/03/2017	13/04/2017	19
Trenching second pass WP1	17/04/2017	30/04/2017	13
Post trenching survey WP 1	30/04/2017	02/05/2017	2
Trenching second pass WP2	03/05/2017	16/05/2017	13
Post trenching survey WP 2	16/05/2017	18/05/2017	2
Cable pull-in (Portgordon)	13/05/2017	18/05/2017	5
Cable lay - campaign 1 (incl. survey)	18/05/2017	02/06/2017	15
Cable pull-in (Noss)	20/06/2017	25/06/2017	5
Cable lay - campaign 2 (incl. survey)	25/06/2017	10/07/2017	15
Cable joint	10/07/2017	17/07/2017	7
Trench backfill	28/07/2017	11/08/2017	14
Post trench backfill survey	11/08/2017	16/08/2017	5
Rock placement (berm)	10/09/2017	19/11/2017	70
Post rock placement survey	19/11/2017	30/11/2017	11
Rock n/s (Noss)	10/09/2017	26/09/2017	16
Rock n/s (Portgordon)	26/09/2017	12/10/2017	16
Post rock n/s survey (Noss)	12/10/2017	13/10/2017	1
Post rock n/s survey (Portgordon)	13/10/2017	15/10/2017	2
Guard vessels (varying quantity)	25/03/2017	30/11/2017	250
